


ID	Task Name	# Business Days	Start	Finish	26 Nov '17	03 Dec '17	10 Dec '17	17 Dec '17	24 Dec '17	31 Dec '17	07 Jan '18									
					M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W
1	<b>RERT Contracts Activated for VIC</b>	1 day	Thu 30/11/17	Thu 30/11/17																
2	RERT Contracts Activation for Billing Week 48 2017	1 day	Thu 30/11/17	Thu 30/11/17																
3	<b>RERT Contracts Deactivated</b>	1 day	Thu 30/11/17	Thu 30/11/17																
4																				
5	AEMO makes provisional determination on compensation amounts (NER 3.12.2)	19 days	Fri 01/12/17	Thu 28/12/17																
6	AEMO issues Final Settlement Statements for Billing Week 48 2017, in accordance with NER 3.15.10C(a)	0 days	Fri 29/12/17	Fri 29/12/17																
7	AEMO notifies Affected Participants of provisional determination on compensation amounts	0 days	Fri 29/12/17	Fri 29/12/17																
8	Affected Participants or Market Customers may seek to vary compensation amount (NER 3.12.2(f))	7 days	Fri 29/12/17	Tue 09/01/18																
9																				
10	<b>If no claims received and Independent Expert is not required...</b>	<b>100 days</b>	<b>Fri 01/12/17</b>	<b>Fri 27/04/18</b>																
11	AEMO makes final determination on compensation amounts (NER 3.12.2)	30 days	Wed 10/01/18	Wed 21/02/18																
12	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days	Fri 02/03/18	Fri 02/03/18																
13	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days	Wed 21/03/18	Wed 21/03/18																
14	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>	<b>Fri 01/12/17</b>	<b>Fri 27/04/18</b>																
15																				
16	<b>If claims received and Independent Expert is not required...</b>	<b>100 days</b>	<b>Fri 01/12/17</b>	<b>Fri 27/04/18</b>																
17	AEMO reviews submissions for additional claims and makes final determination on compensation amounts (NER 3.12.2)	35 days	Wed 10/01/18	Wed 28/02/18																
18	AEMO notifies participants, if claims are accepted, payment will be made in next available billing cycle	10 days	Thu 01/03/18	Wed 14/03/18																
19	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days	Fri 23/03/18	Fri 23/03/18																
20	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days	Fri 13/04/18	Fri 13/04/18																
21	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>	<b>Fri 01/12/17</b>	<b>Fri 27/04/18</b>																
22																				
23	<b>If claims received and Independent Expert is required...</b>	<b>121 days</b>	<b>Wed 10/01/18</b>	<b>Wed 04/07/18</b>																
24	AEMO reviews submissions for additional claims	4 days	Wed 10/01/18	Mon 15/01/18																
25	If claims are not accepted or exceed the amounts under 3.12.2(l), claims are referred to independent expert	0 days	Mon 15/01/18	Mon 15/01/18																
26	AEMO seeks nominations for Independent Expert and advises the market	8 days	Tue 16/01/18	Thu 25/01/18																
27	Referred Participant may object to AEMO's Independent Expert nomination	3 days	Mon 29/01/18	Wed 31/01/18																
28	If objection, AEMO requests that AEMC appoint an Independent Expert	1 day	Thu 01/02/18	Thu 01/02/18																
29	AEMC appoints an Independent Expert	3 days	Fri 02/02/18	Tue 06/02/18																
30	Independent Expert determines value of additional compensation and prepares Draft Report and Assessments	35 days	Wed 07/02/18	Tue 27/03/18																
31	Independent Expert provides Draft Assessment to each Referred Participant and AEMO	1 day	Wed 28/03/18	Wed 28/03/18																
32	AEMO publishes Draft Report on behalf of Independent Expert	1 day	Thu 29/03/18	Thu 29/03/18																
33	AEMO invites submissions from Referred Participants on Draft Report and Assessment on behalf of Independent Expert	0 days	Thu 29/03/18	Thu 29/03/18																
34	Referred Participants submit comments to Independent Expert on Draft Report and Assessment	15 days	Tue 03/04/18	Mon 23/04/18																
35	Referred Participants submit additional information requested by Independent Expert	10 days	Tue 24/04/18	Tue 08/05/18																
36	Independent Expert prepares Final Report and Assessments	15 days	Wed 09/05/18	Tue 29/05/18																
37	Independent Expert provides Final Assessment to each Referred Participant and AEMO	1 day	Wed 30/05/18	Wed 30/05/18																
38	AEMO publishes Final Report on behalf of Independent Expert	1 day	Thu 31/05/18	Thu 31/05/18																
39	AEMO makes final determination on compensation amounts (NER 3.12.2)	10 days	Fri 01/06/18	Thu 14/06/18																
40	AEMO notifies Referred Participants of final determination on compensation amounts	0 days	Fri 15/06/18	Fri 15/06/18																
41	AEMO issues Preliminary Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days	Fri 15/06/18	Fri 15/06/18																
42	AEMO issues Final Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days	Wed 04/07/18	Wed 04/07/18																
43	<b>AEMO must complete final compensation within 150 business days if Independent Expert must determine Participant claim under 3.12.2(f)</b>	<b>150 days</b>	<b>Fri 01/12/17</b>	<b>Fri 06/07/18</b>																

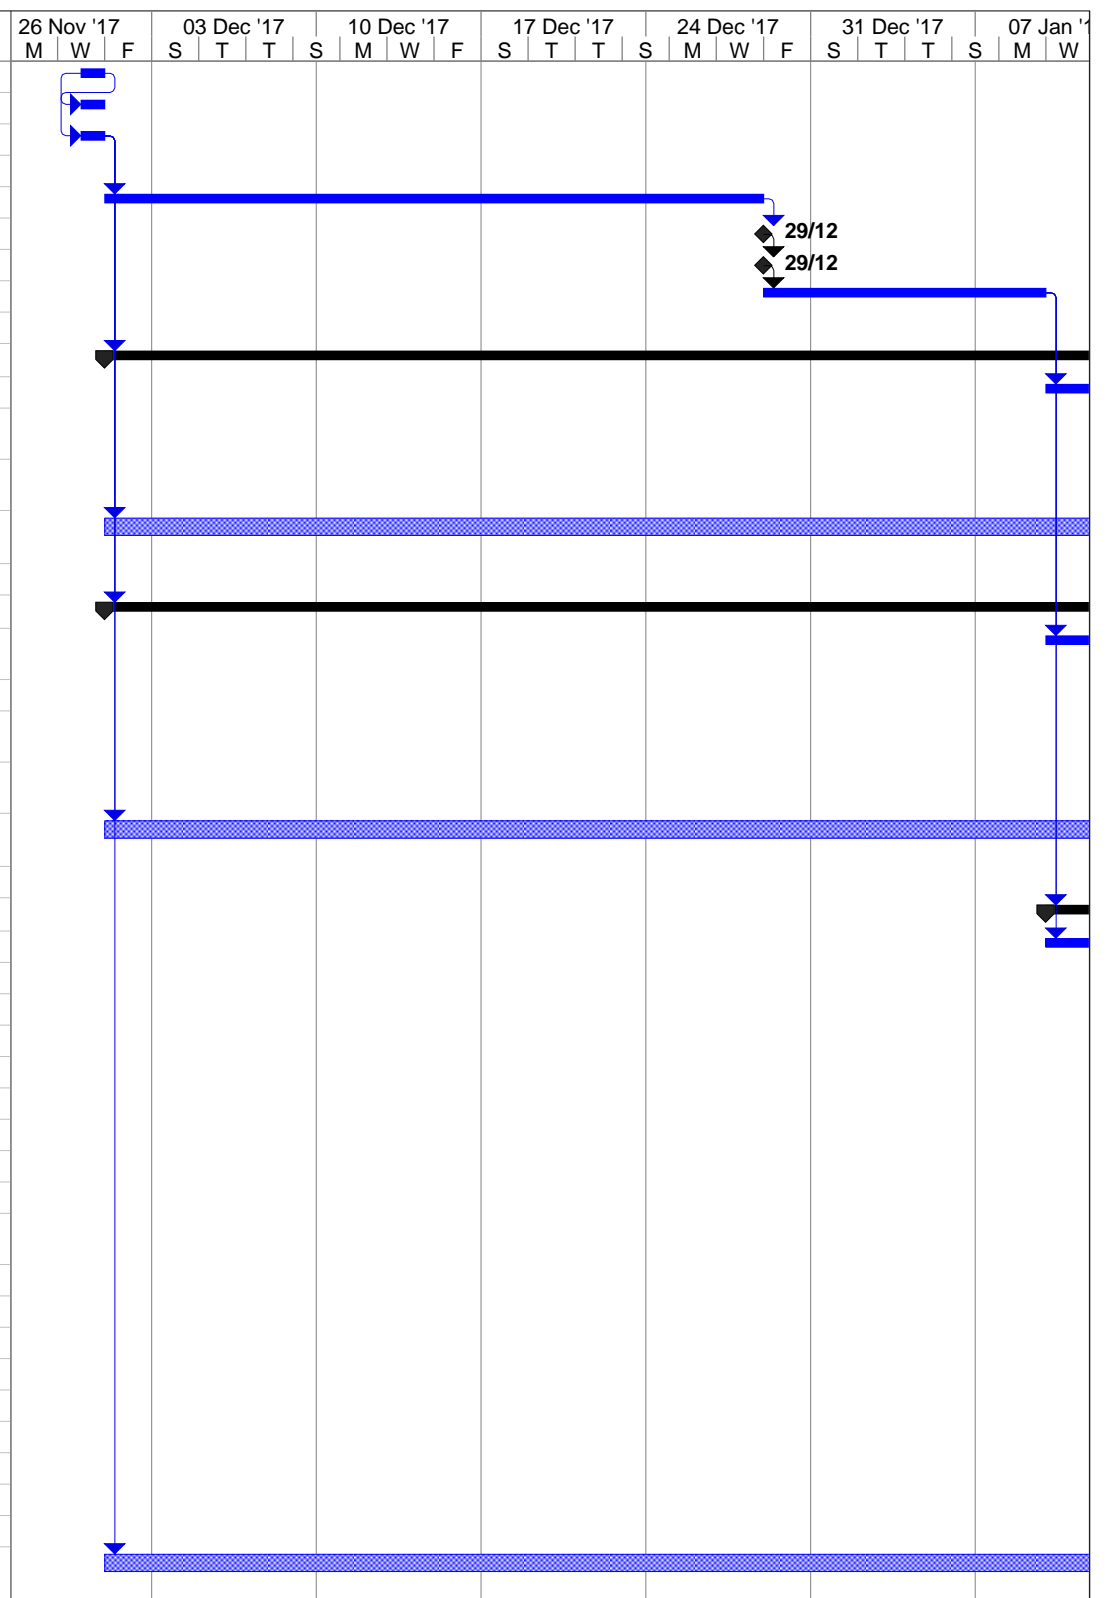

Project: RERT Activation on 30 Nov 2017

Baseline Milestone Detailed Task Summary Baseline   
 Baseline Summary Milestone Task

ID	Task Name	# Business Days	an '18	14 Jan '18	21 Jan '18	28 Jan '18	04 Feb '18	11 Feb '18	18 Feb '18	25 Feb '18	04 Mar '18
			W F	S T T S	M W F	S T T S	M W F	S T T S	M W F	S T T S	M W F
1	<b>RERT Contracts Activated for VIC</b>	1 day									
2	RERT Contracts Activation for Billing Week 48 2017	1 day									
3	<b>RERT Contracts Deactivated</b>	1 day									
4											
5	AEMO makes provisional determination on compensation amounts (NER 3.12.2)	19 days									
6	AEMO issues Final Settlement Statements for Billing Week 48 2017, in accordance with NER 3.15.10C(a)	0 days									
7	AEMO notifies Affected Participants of provisional determination on compensation amounts	0 days									
8	Affected Participants or Market Customers may seek to vary compensation amount (NER 3.12.2(f))	7 days									
9											
10	<b>If no claims received and Independent Expert is not required...</b>	<b>100 days</b>									
11	AEMO makes final determination on compensation amounts (NER 3.12.2)	30 days									
12	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days									
13	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days									
14	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>									
15											
16	<b>If claims received and Independent Expert is not required...</b>	<b>100 days</b>									
17	AEMO reviews submissions for additional claims and makes final determination on compensation amounts (NER 3.12.2)	35 days									
18	AEMO notifies participants, if claims are accepted, payment will be made in next available billing cycle	10 days									
19	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days									
20	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days									
21	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>									
22											
23	<b>If claims received and Independent Expert is required...</b>	<b>121 days</b>									
24	AEMO reviews submissions for additional claims	4 days									
25	If claims are not accepted or exceed the amounts under 3.12.2(l), claims are referred to independent expert	0 days									
26	AEMO seeks nominations for Independent Expert and advises the market	8 days									
27	Referred Participant may object to AEMO's Independent Expert nomination	3 days									
28	If objection, AEMO requests that AEMC appoint an Independent Expert	1 day									
29	AEMC appoints an Independent Expert	3 days									
30	Independent Expert determines value of additional compensation and prepares Draft Report and Assessments	35 days									
31	Independent Expert provides Draft Assessment to each Referred Participant and AEMO	1 day									
32	AEMO publishes Draft Report on behalf of Independent Expert	1 day									
33	AEMO invites submissions from Referred Participants on Draft Report and Assessment on behalf of Independent Expert	0 days									
34	Referred Participants submit comments to Independent Expert on Draft Report and Assessment	15 days									
35	Referred Participants submit additional information requested by Independent Expert	10 days									
36	Independent Expert prepares Final Report and Assessments	15 days									
37	Independent Expert provides Final Assessment to each Referred Participant and AEMO	1 day									
38	AEMO publishes Final Report on behalf of Independent Expert	1 day									
39	AEMO makes final determination on compensation amounts (NER 3.12.2)	10 days									
40	AEMO notifies Referred Participants of final determination on compensation amounts	0 days									
41	AEMO issues Preliminary Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days									
42	AEMO issues Final Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days									
43	<b>AEMO must complete final compensation within 150 business days if Independent Expert must determine Participant claim under 3.12.2(f)</b>	<b>150 days</b>									

Project: RERT Activation on 30 Nov 2017

Baseline Milestone Detailed Task Summary Baseline   
 Baseline Summary Milestone Task

ID	Task Name	# Business Days	11 Mar '18		18 Mar '18			25 Mar '18			01 Apr '18			08 Apr '18			15 Apr '18			22 Apr '18			29 Apr '18			06 May				
			S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F
1	<b>RERT Contracts Activated for VIC</b>	1 day																												
2	RERT Contracts Activation for Billing Week 48 2017	1 day																												
3	<b>RERT Contracts Deactivated</b>	1 day																												
4																														
5	AEMO makes provisional determination on compensation amounts (NER 3.12.2)	19 days																												
6	AEMO issues Final Settlement Statements for Billing Week 48 2017, in accordance with NER 3.15.10C(a)	0 days																												
7	AEMO notifies Affected Participants of provisional determination on compensation amounts	0 days																												
8	Affected Participants or Market Customers may seek to vary compensation amount (NER 3.12.2(f))	7 days																												
9																														
10	<b>If no claims received and Independent Expert is not required...</b>	<b>100 days</b>	[Baseline Milestone]																											
11	AEMO makes final determination on compensation amounts (NER 3.12.2)	30 days																												
12	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days																												
13	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days																												
14	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>	[Baseline Summary]																											
15																														
16	<b>If claims received and Independent Expert is not required...</b>	<b>100 days</b>	[Baseline Milestone]																											
17	AEMO reviews submissions for additional claims and makes final determination on compensation amounts (NER 3.12.2)	35 days																												
18	AEMO notifies participants, if claims are accepted, payment will be made in next available billing cycle	10 days																												
19	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days																												
20	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days																												
21	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>	[Baseline Summary]																											
22																														
23	<b>If claims received and Independent Expert is required...</b>	<b>121 days</b>	[Baseline Milestone]																											
24	AEMO reviews submissions for additional claims	4 days																												
25	If claims are not accepted or exceed the amounts under 3.12.2(l), claims are referred to independent expert	0 days																												
26	AEMO seeks nominations for Independent Expert and advises the market	8 days																												
27	Referred Participant may object to AEMO's Independent Expert nomination	3 days																												
28	If objection, AEMO requests that AEMC appoint an Independent Expert	1 day																												
29	AEMC appoints an Independent Expert	3 days																												
30	Independent Expert determines value of additional compensation and prepares Draft Report and Assessments	35 days																												
31	Independent Expert provides Draft Assessment to each Referred Participant and AEMO	1 day																												
32	AEMO publishes Draft Report on behalf of Independent Expert	1 day																												
33	AEMO invites submissions from Referred Participants on Draft Report and Assessment on behalf of Independent Expert	0 days																												
34	Referred Participants submit comments to Independent Expert on Draft Report and Assessment	15 days																												
35	Referred Participants submit additional information requested by Independent Expert	10 days																												
36	Independent Expert prepares Final Report and Assessments	15 days																												
37	Independent Expert provides Final Assessment to each Referred Participant and AEMO	1 day																												
38	AEMO publishes Final Report on behalf of Independent Expert	1 day																												
39	AEMO makes final determination on compensation amounts (NER 3.12.2)	10 days																												
40	AEMO notifies Referred Participants of final determination on compensation amounts	0 days																												
41	AEMO issues Preliminary Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days																												
42	AEMO issues Final Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days																												
43	<b>AEMO must complete final compensation within 150 business days if Independent Expert must determine Participant claim under 3.12.2(f)</b>	<b>150 days</b>	[Baseline Summary]																											

Project: RERT Activation on 30 Nov 2017

Baseline Milestone ◊      Detailed Task █      Summary ▬      Baseline ▬  
 Baseline Summary ▬      Milestone ◆      Task ▬

ID	Task Name	# Business Days	11 May '18		13 May '18				20 May '18				27 May '18				03 Jun '18				10 Jun '18				17 Jun '18				24 Jun '18				01 Jul '18			
			T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S	M	W	F	S	T	T	S				
1	<b>RERT Contracts Activated for VIC</b>	1 day																																		
2	RERT Contracts Activation for Billing Week 48 2017	1 day																																		
3	<b>RERT Contracts Deactivated</b>	1 day																																		
4																																				
5	AEMO makes provisional determination on compensation amounts (NER 3.12.2)	19 days																																		
6	AEMO issues Final Settlement Statements for Billing Week 48 2017, in accordance with NER 3.15.10C(a)	0 days																																		
7	AEMO notifies Affected Participants of provisional determination on compensation amounts	0 days																																		
8	Affected Participants or Market Customers may seek to vary compensation amount (NER 3.12.2(f))	7 days																																		
9																																				
10	<b>If no claims received and Independent Expert is not required...</b>	<b>100 days</b>																																		
11	AEMO makes final determination on compensation amounts (NER 3.12.2)	30 days																																		
12	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days																																		
13	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days																																		
14	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>																																		
15																																				
16	<b>If claims received and Independent Expert is not required...</b>	<b>100 days</b>																																		
17	AEMO reviews submissions for additional claims and makes final determination on compensation amounts (NER 3.12.2)	35 days																																		
18	AEMO notifies participants, if claims are accepted, payment will be made in next available billing cycle	10 days																																		
19	AEMO issues Preliminary Settlement Statements with final determination, and notifies Affected Participants on compensation amounts	0 days																																		
20	AEMO issues Final Settlement Statements with the final determination, and notifies Affected Participants on compensation amounts	0 days																																		
21	<b>AEMO must complete final compensation within 100 business days if Independent Expert is not required</b>	<b>100 days</b>																																		
22																																				
23	<b>If claims received and Independent Expert is required...</b>	<b>121 days</b>																																		
24	AEMO reviews submissions for additional claims	4 days																																		
25	If claims are not accepted or exceed the amounts under 3.12.2(l), claims are referred to independent expert	0 days																																		
26	AEMO seeks nominations for Independent Expert and advises the market	8 days																																		
27	Referred Participant may object to AEMO's Independent Expert nomination	3 days																																		
28	If objection, AEMO requests that AEMC appoint an Independent Expert	1 day																																		
29	AEMC appoints an Independent Expert	3 days																																		
30	Independent Expert determines value of additional compensation and prepares Draft Report and Assessments	35 days																																		
31	Independent Expert provides Draft Assessment to each Referred Participant and AEMO	1 day																																		
32	AEMO publishes Draft Report on behalf of Independent Expert	1 day																																		
33	AEMO invites submissions from Referred Participants on Draft Report and Assessment on behalf of Independent Expert	0 days																																		
34	Referred Participants submit comments to Independent Expert on Draft Report and Assessment	15 days																																		
35	Referred Participants submit additional information requested by Independent Expert	10 days																																		
36	Independent Expert prepares Final Report and Assessments	15 days																																		
37	Independent Expert provides Final Assessment to each Referred Participant and AEMO	1 day																																		
38	AEMO publishes Final Report on behalf of Independent Expert	1 day																																		
39	AEMO makes final determination on compensation amounts (NER 3.12.2)	10 days																																		
40	AEMO notifies Referred Participants of final determination on compensation amounts	0 days																																		
41	AEMO issues Preliminary Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days																																		
42	AEMO issues Final Settlement Statements with the final determination, in accordance with NER 3.15.10C(b)	0 days																																		
43	<b>AEMO must complete final compensation within 150 business days if Independent Expert must determine Participant claim under 3.12.2(f)</b>	<b>150 days</b>																																		

Project: RERT Activation on 30 Nov 2017

Baseline Milestone ◊      Detailed Task █      Summary █      Baseline █  
 Baseline Summary █      Milestone ◆      Task █
